US Army Corps
of Engineers

FEMA

USACE/FEMA 2008 RAP Workshop

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Briefing Order:

- **Interagency Operational Planning**
- **Response Organization**
- **Mission Assignment**
- **Temporary Power**
- **Commodities and Logistics**
- **Critical Infrastructure Assessment**
- **Temporary Housing and Roofing**
- **Flood Risk Management**

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Interagency Operational Planning

Breakout Outbrief

Pre-Disaster Interagency Deliberate/Contingency Planning

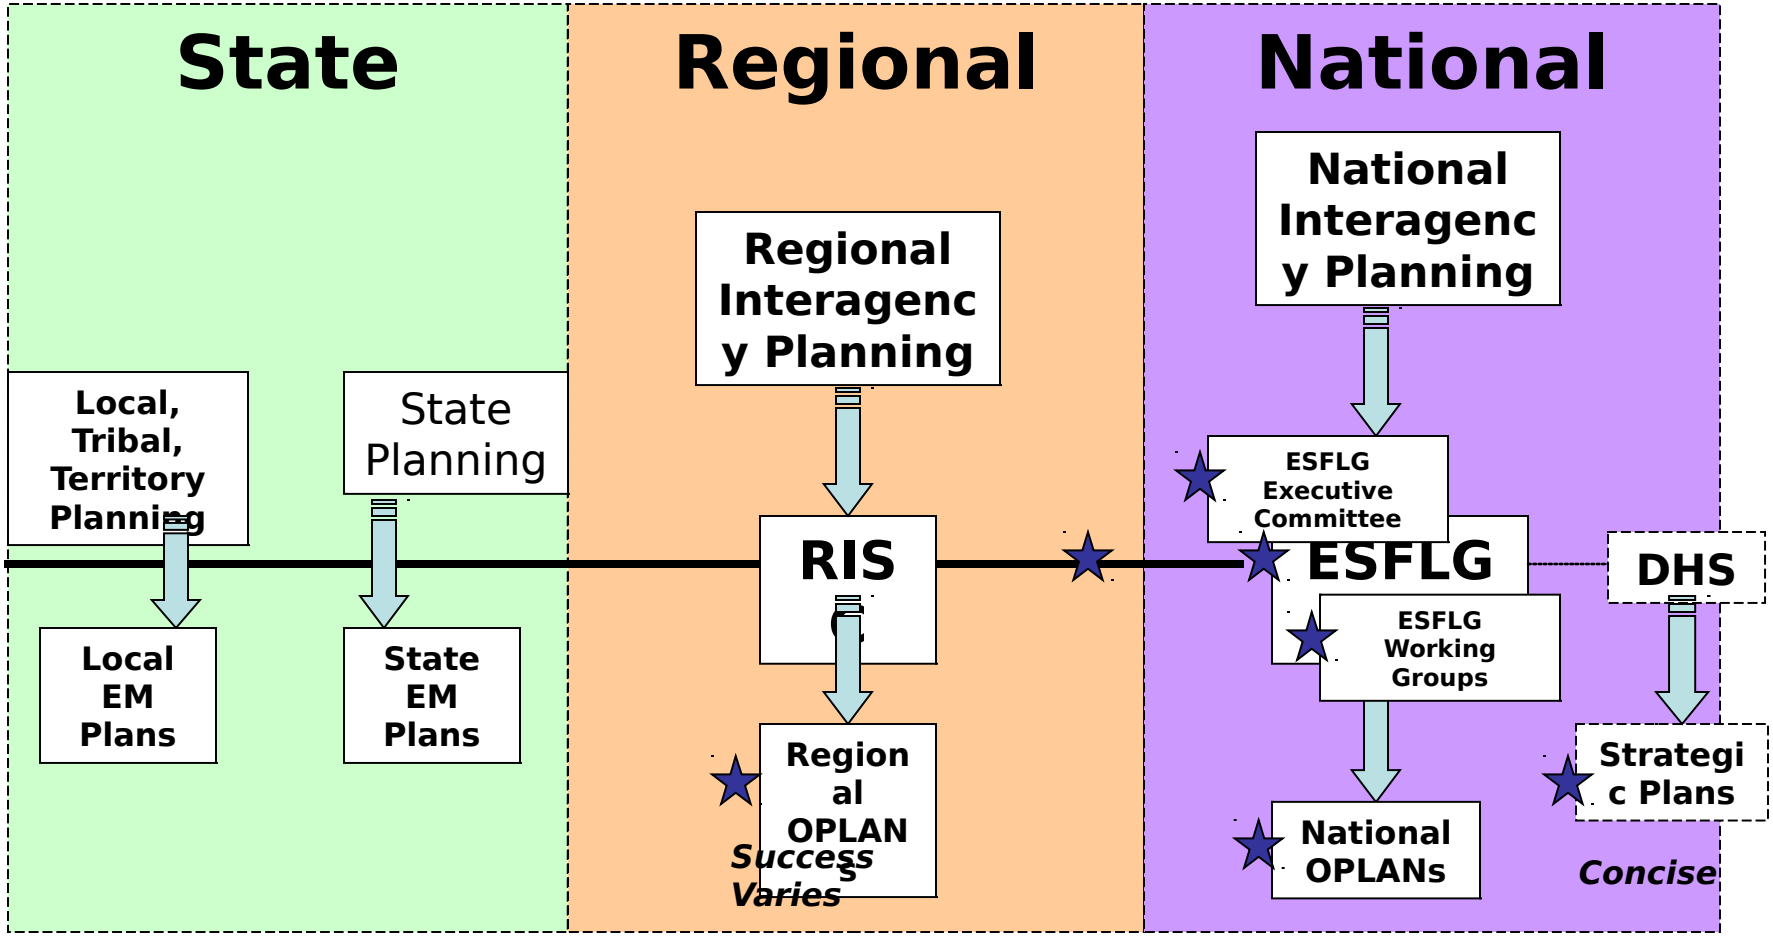

★ = Gap or Issue

Created by Erik Wozniak, FEMA HQ Ops

Post Disaster Interagency Planning

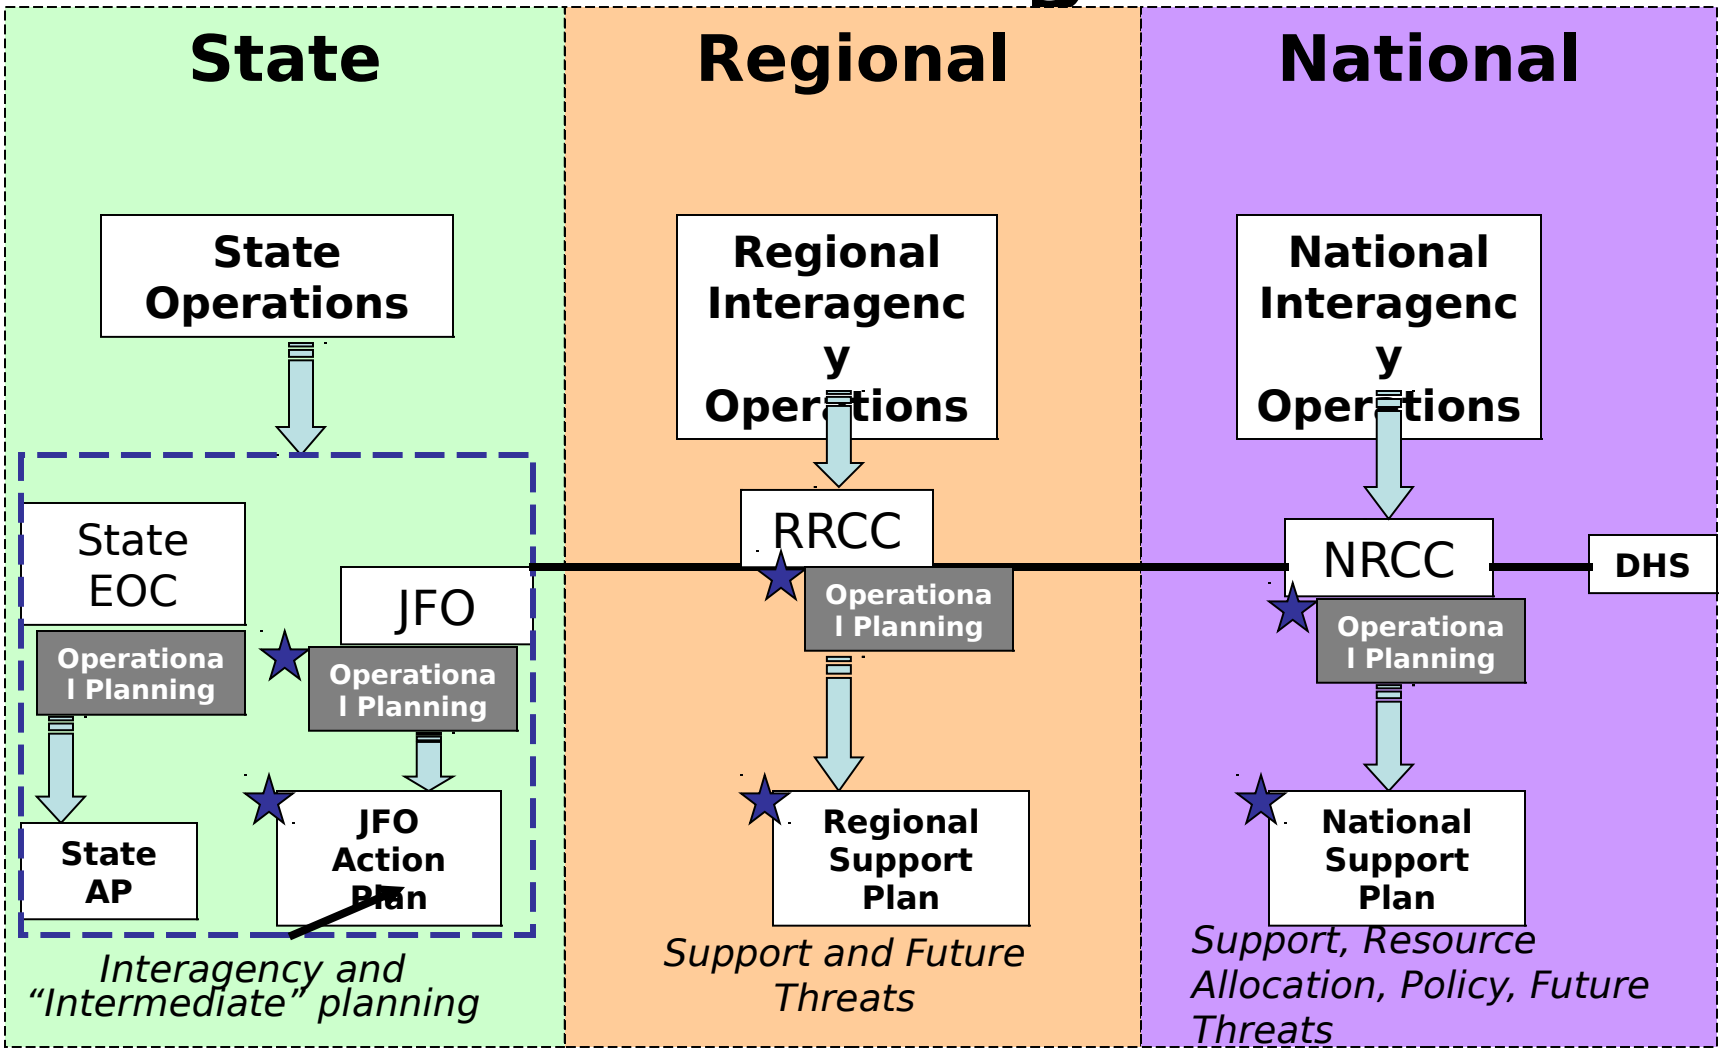

US Army Corps of Engineers

Interagency Operational Planning – Deliberate Planning

FEMA

Issue:	Proposed COA / Timeline	Lead/PDT
Federal doctrine for deliberate planning is not widely understood, and is not being effectively implemented. **Priority:** *Short-Term/ Long-Term* **Obstacles:** Time, Funding & Resources	- Recommend to new leadership to support and resource IPS and revise implementation to ensure realistic and effective results. *(February 2009)* - Develop strategy for awareness and training on the Integrated Planning System (IPS). (*Tentative: February 2009*) - Establish hierarchy for existing and identified operational planning doctrine documents and plans, and how they nest. (*March 2009*) - Identify methods, best practices, and planning tools for deliberate planning processes and share with partners	**Proposed Lead:** FEMA HQ Operational Planning Branch with Interagency Partners

US Army Corps of Engineers

Interagency Operational Planning – Crisis Action Planning

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
Federal interagency community is unable to implement a comprehensive federal <u>crisis-action planning</u> system. **<u>Priority</u>:** *Short-Term/Long-Term* **<u>Obstacles</u>:** Time, Funding,	- Better define the roles and responsibilities for crisis-action planning between vertical levels (e.g., JFO – RRCC – NRCC). (*June 2009*) - Develop common priorities to synchronize crisis-action planning efforts both vertically and horizontally. (*June 2009*) - Develop strategy for awareness and training on federal interagency crisis-action planning. (*June 2009*) - Need to determine linkages and transitions between crisis-action plans and both short-term and long-term recovery plans. (*December 2009*)	**<u>Proposed Lead:</u>** FEMA HQ Operational Planning Branch with Interagency Partners

US Army Corps of Engineers

Interagency Operational Planning

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
The linkages between deliberate planning and crisis-action planning are not sufficiently defined. **Priority:** *Short-Term* **Obstacles:** Vetting/Approval of Doctrine	- Identify key concepts and integration approaches for presentation to the Senior Leaders at the April 2009 Senior Leaders' Seminar. (*April 2009*) - Will also be addressed by recommendations under first 2 issues.	**Proposed Lead:** FEMA HQ Operational Planning Branch with Interagency Partners

Interagency Operational Planning Relationships

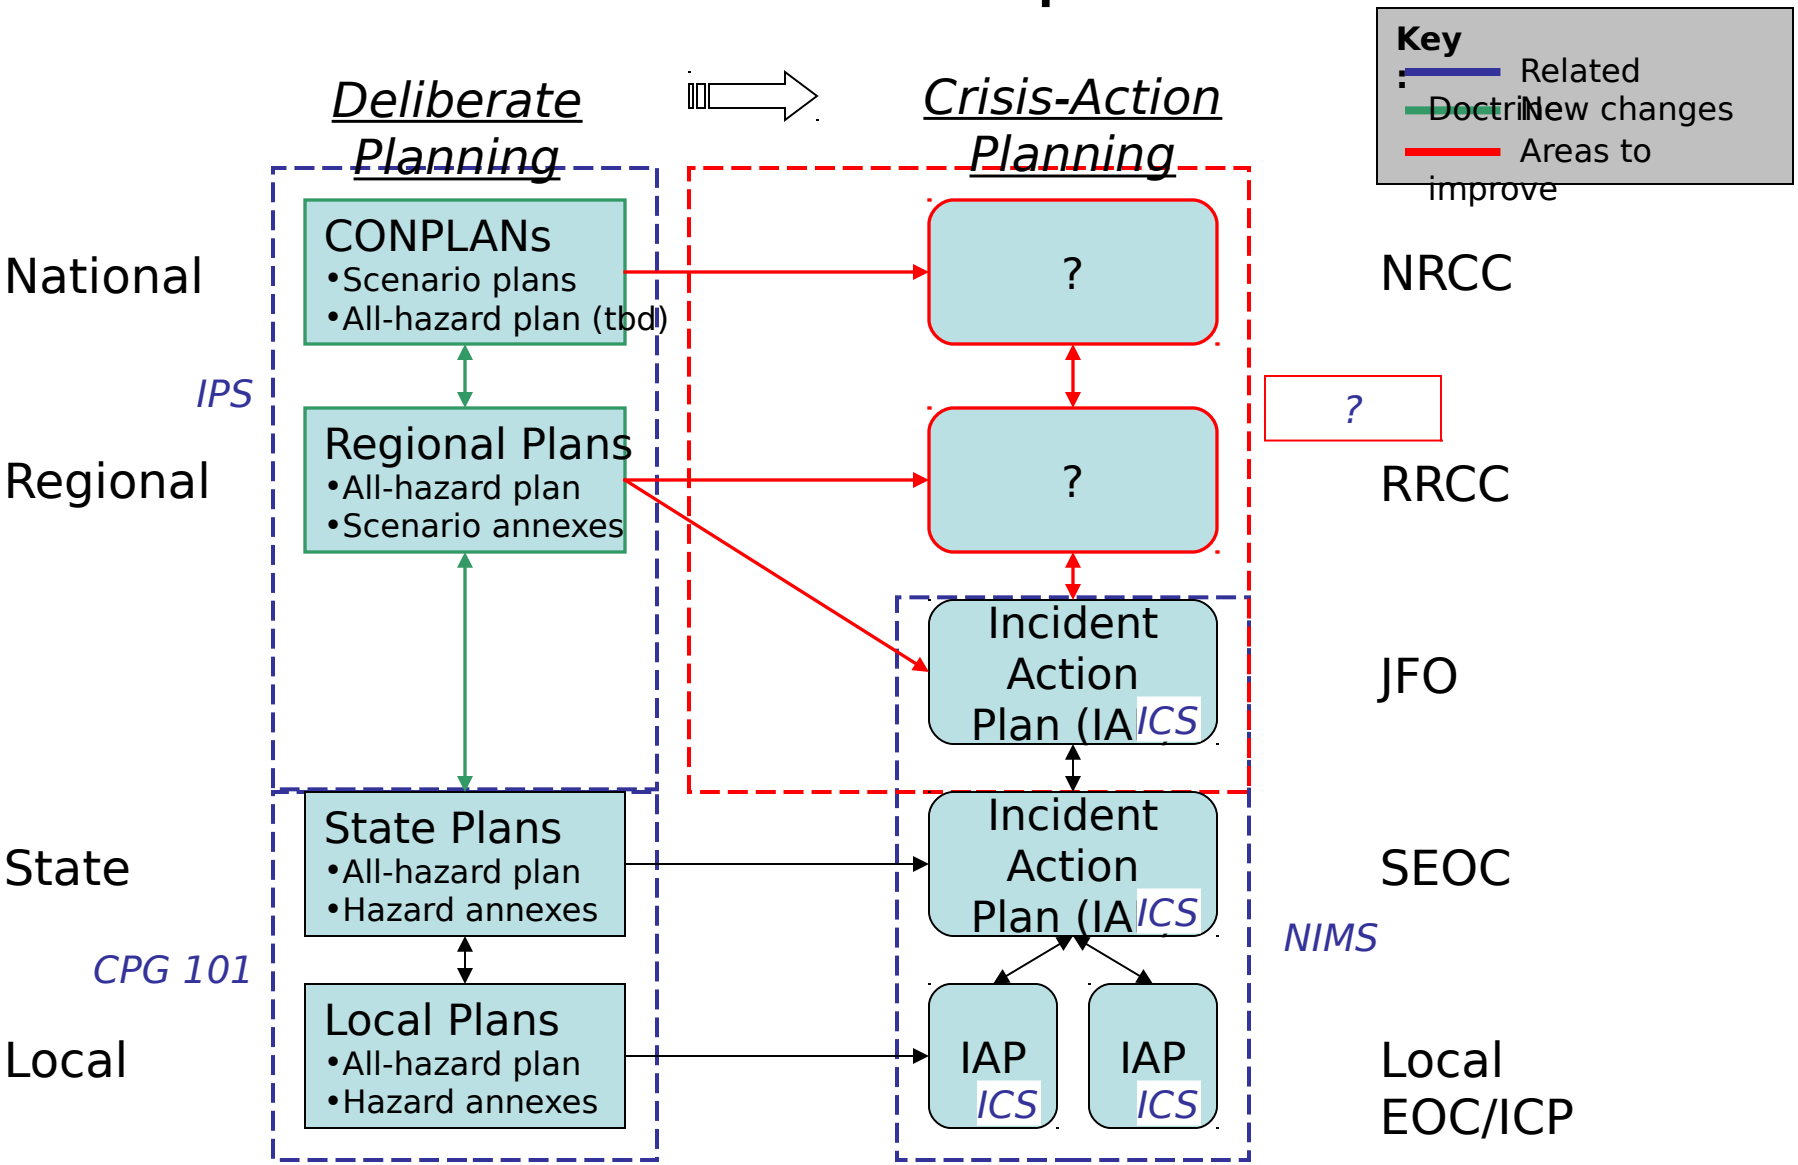

Created by Erik Wozniak, FEMA HQ Ops

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

Interagency Operational Planning Breakout Outbrief

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Response Organization Out-brief

US Army Corps of Engineers

Response Organization Role

FEMA

Issue: 1	Proposed COA/Timeline	Lead/PDT
Lack of guidance in utilizing IMAT's within the response CONOPS **Priority: Short Term**	**Dates:** 01-JUN-2009 Modify existing draft IMAT CONOPS to in include roles, responsibilities, and authorities at the JFO/AFO, Branch and Division levels. Share with stake holders: RISC, TL/ATL, LGL, ESFLG, **Obstacles:** Approval of final document	**PDT Lead:** **FEMA – Mark Wheatley** **PDT Members:** **USACE:** **Allen Morse** **FEMA:** **Ginger Edwards, Holly Hollingsworth Mike Hall**

US Army Corps of Engineers

Response Organization Role

FEMA

Issue: 2	Proposed COA/Timeline	Lead/PDT
Lack of guidance/doctrine within the JFO manual concerning roles/responsibilities at Branches/Divisions (AFO) level. **Priority: Short Term**	**Dates:** 01-JUN-2009 (annex) -Propose as annex to JFO Manual -Train stake holders -Identify types of AFOs -Tasking authority **Obstacles:** New doctrine development	**PDT Lead:** **FEMA – Jennifer Rosenberger** **PDT Members:** **USACE:** **Kelley Aasen** **FEMA:** **Phil Parr** **Jeff Lusk** **Lauren Mclane**

US Army Corps of Engineers

Response Organization Role

FEMA

Issue: 3	Proposed COA/Timeline	Lead/PDT
Identify reporting requirements at the FEMA division and branch level **Priority: Short Term**	**Dates:** 01-JUN-2009 **Identify requirements** **Modify reporting systems if necessary** **Train Teams** **Obstacles:** Change to current systems	**PDT Lead:** **USACE – A. Morse** **PDT Members:** **USACE:** **Kelley Aasen** **Russ Jaramillo** **FEMA:** **Phill Parr** **Jeff Lusk** **Ginger Edwards**

US Army Corps of Engineers

Response Organization Role

FEMA

Issue: 4	Proposed COA/Timeline	Lead/PDT
No full time dedicated ESF#3 TL, OFA support to the IMAT's **Priority: Long Term**	**Dates:** unknown Provide full time support to the IMAT's Bring forth to ESFLG Key regions **Fund ½ FTE** **Obstacles:** Funding	**PDT Lead:** **USACE HQ** **FEMA HQ** **PDT Members:**

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

RESPONSE ORGANIZATION ROLES

Breakout Outbrief

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Mission Assignment Out-brief

US Army Corps of Engineers

Mission Assignment Breakout

FEMA

Issue: Process	Proposed COA/Timeline	Lead/PDT
1. *Lack of Standardization of the MA Process* ***2.*** *Limited visibility into the tracking and status of an ARF and MA* ***3.*** *Clarification and expectations of the closeout process* **Priority:** Short Term 1 Jun 09	**1. Recommended solutions:** • Establish a MA Section • Establish a workforce management process • Establish a DAE MA Cadre • Document end-to-end process • Define roles and responsibilities **2. Recommended solutions:** • Automate the ARF process • Put a tracking system in place • Establish a good reporting process (i.e., EMIMS) **3. Recommended solutions:** • Proper coordination • Document the process • Increase education and training on the process **Obstacles:**	**PDT Lead:** FEMA/USACE **PDT Members (Initial):** Lisa Maddry (FEMA) Lisa Bordeaux (USACE) Muriel Glover (FEMA) Liz Miller (USACE) Marc Bergman (USACE) Harold Washington (FEMA) Regional personnel Designated partner agencies

US Army Corps of Engineers

Mission Assignment Breakout

FEMA

Issue: Training	Proposed COA/Timeline	Lead/PDT
1. *Not enough qualified MA staff* ***2.*** *No clear understanding of the MA process (across FEMA and OFAs)* ***3.*** *eCAPS Coding (i.e., DFA is default in eCAPS)* **Priority:** Short/Long Term Incremental	**1. Recommended solution:** • Establish a cadre of qualified (i.e., certification) MA staff **2. Recommended solution**: • Provide more training on the MA process **3. Recommended solutions**: • Clearly define in the ARF SOW and PSMA if it is a DFA, TA, or FOS • Currently being worked in eCAPS • Provide more training in eCAPS **Obstacles:** Funding, Staffing (Hiring)	**PDT Lead:** FEMA/USACE **PDT Members (Initial):** Lisa Maddry (FEMA) Lisa Bordeaux (USACE) Muriel Glover (FEMA) Liz Miller (USACE) Marc Bergman (USACE) Harold Washington (FEMA) Regional personnel Designated partner agencies

US Army Corps of Engineers

Mission Assignment Breakout

FEMA

Issue: Finance	Proposed COA/Timeline	Lead/PDT
1. *Lack of visibility into the coordination process when closing out a MA* ***2.*** *There is difficulty changing funding accounts in eCAPS when transitioning from Emergency to Major Declarations* ***3.*** *Confusion over operationally complete and financially complete MAs.* **Priority:** Short Term 1 Jun 09	**1. Recommended solution:** • Increased communication **2. Recommended solution:** • Review and document the process/system requirements and feasibility • Change IFMIS process **3. Recommended solution:** • Designated closeout POC • Establish a closeout team • Document the process **Obstacles:** IT and CFO impact	**PDT Lead:** FEMA/USACE **PDT Members (Initial):** Lisa Maddry (FEMA) Lisa Bordeaux (USACE) Muriel Glover (FEMA) Liz Miller (USACE) Marc Bergman (USACE) Harold Washington (FEMA) Regional personnel Designated partner agencies

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

Mission Assignment Breakout Outbrief

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Emergency Power Out-brief

US Army Corps of Engineers

Emergency Power

FEMA

Issue: Staging Areas	Proposed COA/Timeline	Lead/PDT
Coordination with respect to Pre-Dec (NLSA) and Post-Dec (LSA) staging areas can be improved to enhance initial mobilization and mission execution. **Priority:** *Immediate*	**COA:** 1. LRP will participate in FEMA LOG Pre-Dec conference call to ensure appropriate power response requirements are provided and NLSA/LSA locations are coordinated. 2. LRP will participate in monthly LOG conference calls during "peace time" to ensure preparedness. **Dates:** April 2009 **Obstacles:** None	**PDT Lead:** Fichera (USACE) Southerland (FEMA) Hoban (FEMA) **PDT Members:** FEMA Region Log

US Army Corps of Engineers

Emergency Power

FEMA

Issue: FEMA Power-Pack	Proposed COA/Timeline	Lead/PDT
Existing FEMA "Power or 50-pack" needs altered to ensure initial push of generators has sufficient capability to meet customer's needs. Recent missions illustrate the need for larger gens at onset of mission. **Priority:** *Immediate* **Obstacles:** COA 1: Cultural change at DC's COA 2: None COA 3: Funds to procure BOM if needed	**COA:** 1. 249th/LRP will develop a new "power pack" configuration which will provide increased capability. 2. New "power pack" designation will also be "NIMS" compliant. 3. Associated BOM will also be determined to match new "power pack" and be NIMS compliant. 4. Power COP will develop augmented list of gens for each "notice" event based on "GAP" and previous PII's. **Dates:** Feb 2009	**PDT Lead:** Hall (249th) Southerland (FEMA) **PDT Members:** FEMA Region Log Fichera (USACE) FEMA DC's

US Army Corps of Engineers

Emergency Power

FEMA

Issue: Inter-Agency Task Force	Proposed COA/Timeline	Lead/PDT
The power task force and FEMA LOG "fly away team" concept worked exceptionally well during the Ike Response. This has/will enhance comms, streamline resource ordering, and strengthen situational awareness. **Priority:** *Immediate*	**COA:** 1. FEMA LOG to solidify concept and develop "fly away team" SOP. 2. USACE/FEMA to solidify concept, positions and develop "task force" SOP. **Dates:** Feb 2009 **Obstacles:** COA 1: None COA 2: None	**PDT Lead:** Navesky (USACE) Backe (USACE) Hoban (FEMA) Kaczorowski (FEMA) **PDT Members:** LRP, LRD, ULA, FEMA LOG, NRCC, NAP KO

US Army Corps of Engineers

Emergency Power

FEMA

Issue: Exercise Planning	Proposed COA/Timeline	Lead/PDT
Better inter-agency coordination is needed to ensure the emergency power COP takes full advantage of state, regional, and national exercises. **Priority:** *Short Term*	**COA:** 1. DEM's coordinate possible Region Exercises with LRD for potential power engagement. 2. USACE LNO at FEMA HQ to coordinate potential power related exercises to LRD. 3. USACE/FEMA develop annual "cross-talk" of current and next FY exercises which may engage emergency power COP. **Dates:** Feb 2009 **Obstacles: None**	**PDT Lead:** Porter (USACE) Navesky (USACE) Munoz (FEMA) **PDT Members:** FEMA Region DOD's, DAD's and NPD's Navesky (USACE) DEM's (USACE)

US Army Corps of Engineers

Emergency Power

FEMA

Issue: Cold Weather Mission Execution	Proposed COA/Timeline	Lead/PDT
Current FEMA inventory of generators is not conducive to “cold weather” (<25 F) operation. **Priority:** *COA 1: Immediate* *COA 2: Immediate* *COA 3: Long Term*	**COA:** 1. USACE to develop initial “power pack” of gens for “cold weather” areas based on previous exercises PII’s (AK). 2. 249th to perform “gap analysis” of what is needed to augment current gen inventory to operate in cold environment. 3. FEMA purchase additional cold weather components and develop cold weather power pack. **Dates:** FY 2010 **Obstacles:** COA 1: none COA 2: none COA 3: Funding/inventory	**PDT Lead:** FEMA LOG **PDT Members:** 249th Navesky (USACE) Power SMEs POD EM

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

Emergency Power Outbrief

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Logistics/Commodity Out-brief

US Army Corps of Engineers

Logistics/Commodity

FEMA

Issue: 1	Proposed COA/Timeline	Lead/PDT
National Logistics Staging Area (NLSA) resource requirements are not clearly identified. **Priority:** Immediate	**Dates:** 01 Feb 09 Clarify and finalize requirements, acquire equipment, identify and appoint staffing, finalization of NLSA doctrine, vet with partners **Obstacles:** Limited funding, availability of personnel and support from Regions to release trained staff.	**PDT Lead:** Shawn Matz-FEMA **PDT Members:** FEMA Jeff Bezore John Gossman USACE Gretchen Martinsen Mike Keegan Gary Stangeland

US Army Corps of Engineers

Logistics/Commodity

FEMA

Issue: 2	Proposed COA/Timeline	Lead/PDT
There is a lack of single source doctrine that outlines the Federal, State, and Local agency roles and responsibilities with regard to resource distribution during contingency operations. **Priority: Short-Term**	**Dates:** Target - 01 March 09 DMSWG to provide national sourcing plan to partners, establish shared document site for Regional and state specific annexes. **Obstacles:** Level of documentation varies between Regions and not all have developed to the level Regions 4 and 6.	**PDT Lead:** Robert Hill-FEMA **PDT Members:** FEMA Scott Erickson Kertz Hare Kent Weathers Other Regional Logistics Chiefs

US Army Corps of Engineers

Logistics/Commodity

FEMA

Issue: 3	Proposed COA/Timeline	Lead/PDT
There is an inconsistent level of logistical planning and execution capabilities at the state level. **Priority:** Long Term	**Dates: Beyond 1 June 09** **Need to make technical assistance and funding source for Logistical Planning available at the state level.** **-Implement TA Contract at HQ FEMA level. Follow model used for evacuation planning to provide direct assistance to the state.** **-Establish incentives for Log Planning and execution initiatives** **Obstacles: Funding, legislation, state and local laws and policies. No required National Standard**	**PDT Lead:** Shawn Matz-FEMA **PDT Members:** Florida: Chuck Hagan FEMA Mary Anne Lyle, FEMA Plans and Exercises Division, Region 4 and 6 logistics staff.

US Army Corps of Engineers

Logistics/Commodity

FEMA

Issue: 4	Proposed COA/Timeline	Lead/PDT
There is a lack of a formalized Point of Distribution (POD) Training available to the states. **Priority:** Immediate & Long Term Initiative **(Incremental)**	**Dates:** 01 March 09 Develop and deploy a POD Training Road show and resource the initiative to provide formalized training to appropriate state and local responders. **Obstacles:** Funding for intergovernmental efforts.	**PDT Lead:** **Shawn Matz-FEMA** **PDT Members:** **FEMA** **Jackie Gladish** **Kent Weathers** **Scott Erickson** **Amelia Weathers** **Emergency Management Institute** **Rich Kaiser** **USACE** **Gretchen Martinsen Drew Benziger** **Readiness Support Center**

US Army Corps of Engineers

Logistics/Commodity

FEMA

Issue: 5	**Proposed COA/Timeline**	**Lead/PDT**
There is a lack of a comprehensive resource tracking capability between partner agencies. **Priority:** Short Term, Long Term, Incremental	**Dates:** 01 Feb 09 Establish PDT to accomplish on-boarding of partner data to enhance Total Asset Visibility **Obstacles:** Funding, system interface	**PDT Lead:** Mary Rose Register **PDT Members:** USACE Mike Keegan Pat O'Donnell Holmes Walters FEMA Mark Raiffa

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

Logistics/Commodity Breakout Outbrief

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Critical Infrastructure Assessment and Restoration

Out-brief

US Army Corps of Engineers

Critical Infrastructure Assessment and Restoration

FEMA

Issue: *CIA&R-1*	**Proposed COA/Timeline**	**Lead/PDT**
SWEAT analysis: Sewer, Water, Electrical, Academics & Trash What is the best method of performing for SWEAT analysis? **Priority:** Short -Term	**Dates:** 1 June 2009 **Recommendation:** Utilize SWEAT doctrine developed by the Army with modifications for civil disasters **Obstacles:** Education of intergovernmental agencies and formation of SWEAT Teams	**PDT Lead:** USACE IMAT Lead with support from FEMA IMAT **PDT Members:** TBD

US Army Corps of Engineers

Critical Infrastructure Assessment and Restoration

FEMA

Issue: CIA&R-2	Proposed COA/Timeline	Lead/PDT
Better collaboration between EPA and ESF #3 on water and wastewater Mission Assignments during disasters. **Priority:** Short-term	**Dates:** 1 June 2009 **Recommendations:** -USACE and EPA co-host a dedicated workshop -Develop SOPs in collaboration with FEMA -Incorporate into ESF #3 doctrine -Use the results as a template for other ESF #3 support agencies. **Obstacles:**	**PDT Lead:** Jack Hurdle Kevin Tingley **PDT Members:** TBD

US Army Corps of Engineers

Critical Infrastructure Assessment and Restoration

FEMA

Issue: CIA&R-3	Proposed COA/Timeline	Lead/PDT
Private sector entities, providing a life sustaining public service (ex. Private water systems) do not qualify for Federal assistance. **Priority:** Immediate to Short term	**Dates:** 1 June 2009 **Recommendation:** Establish policy that allows Federal assistance for emergency protective measures for private (for profit) entities that provide life sustaining services **Obstacles:** Reluctance of leadership to endorse recommendation	**PDT Lead:** FEMA-PA? **PDT Members:** TBD

US Army Corps of Engineers

Critical Infrastructure Assessment and Restoration

FEMA

Issue: CIA&R-4	Proposed COA/Timeline	Lead/PDT
IT Inter-operability **Priority:** Short term	**Dates:** 1 June 2009 **Recommendations:** -Interagency team to solve interoperability of Automated Information System -IT solutions need to allow non-federal agencies with a need to know access. -Geo-Spatial standards need to be established	**PDT Lead:** Interagency Senior Leaders drive the IT solution **PDT Members:** TBD

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

Critical Infrastructure Assessment and Restoration Breakout Out-brief

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Temporary Housing and Roofing Out-brief

US Army Corps of Engineers

Temporary Housing and Roofing

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
TH&R-1: USACE role in housing mission remains indefinite and requests for support vary throughout the spectrum of housing options. **<u>Priority</u>: 2 for most, 1 for number 4.**	**Dates:** **1. Draft comprehensive Concept of Operations by 1 Apr 09.** **2. USACE continues current level of disaster support through hurricane season 2009.** **3. FEMA evaluates requirements for USACE support during 2009.** **4. USACE to re-evaluate non-disaster support FEMA HQ by 31 Jan.**	**<u>PDT Lead:</u>** **1. FEMA/Rave** **2. No requirement** **3. FEMA/Rave** **4. USACE /Fletcher** **<u>PDT Members:</u>** **To be determined by leads**

US Army Corps of Engineers

Temporary Housing and Roofing

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
TH&R-2: FEMA may exercise the option of assigning full housing mission assignment to USACE to include contracting for haul & install and community site development. **<u>Priority</u>: 1 for all, due dates all 01 Jun 09**	**Dates:** **1. Identify parameters to determine if USACE or IA-TAC would be assigned a mission.** **2. FEMA would retain maintenance and deactivation.** **3. Have USACE investigate setting up ACI Contract. Would not be awarded**	**<u>PDT Lead:</u>** **FEMA / Jonathan Torres** **USACE / Fletcher** **<u>PDT Members:</u>** **To be determined by leads**

US Army Corps of Engineers

Temporary Housing and Roofing

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
TH&R-3: There is no standardized training for housing personnel between the agencies. **<u>Priority</u>: 2 except for number 1.**	**Dates:** **1. USACE sponsors Housing PRT training June 2009.** **2. Develop joint FEMA/USACE training.** **3. Identify exercise opportunities for FEMA/USACE, local and regional partners.**	**<u>PDT Lead:</u>** **USACE Premo - Fletcher – Kolditz** **FEMA Rave and Jones** **<u>PDT Members:</u>** **To be determined by leads**

US Army Corps of Engineers

Temporary Housing and Roofing

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
TH&R-4: Electrical hook-ups and local inspections continue to delay lease-in process. **Priority: 2**	**Dates:** **1. FEMA will develop field operational guidance to improve coordination of electrical and utilities issues. Tasks include: Evaluate systems delivery, capability of local utilities, identification of code inspection requirements, "call before you dig" requirements, role of state.** **Obstacles:**	**PDT Lead:** **FEMA Rave** **PDT Members:** **FEMA, National Disaster Housing Task Force, USACE, Office of Private Sector and DOE.**

US Army Corps of Engineers

Temporary Housing and Roofing

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
TH&R-5: Continued development of National Coverage Policy to include Critical Public Facilities **<u>Priority</u>: 2 except for the last which is on-going thus priority 3**	**Dates:** **1. Standardize the Event Policy into a National Policy.** **2. Provide clarity to USACE regarding coverage and building types.** **3. Develop fact sheet for state and local officials describing the roofing program,** **4. Redo Blue Roof video** **5. Continue to identify alternative**	**<u>PDT Lead:</u>** **1. and 2. FEMA IA and PA - Joan Rave and PA tbd.** **3. USACE – Murrell** **4. USACE - Lynch with USACE FEMA – Rave** **5. USACE - Murrell** **<u>PDT Members:</u>** **To be determined**

US Army Corps of Engineers

Temporary Housing and Roofing

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
TH&R 7 - Use of VOLAGs (volunteer agencies) on the Temporary Roofing Mission. (TH&R 6 is USACE only) **Priority: 2**	**Dates:** **USACE will develop VOLAG SOP or MOA for registered volunteer groups. This can be done during SOP week in January 2009.** **Obstacles:**	**PDT Lead:** **USACE - Murrell** **PDT Members:** **To be determined by leads.**

US Army Corps of Engineers

Temporary Housing and Roofing

FEMA

Issue:	Proposed COA/Timeline	Lead/PDT
TH&R-8: Rapid Ramp up of Temporary Roofing Mission. **<u>Priority</u>: 2**	**Dates:** **1. USACE drafts new pre-scripted mission assignment.** **2. Identify existing local district contracts ROE and QA** **3. Develop new QA training and add QA Trainers to PRT.** **4. Add ROE Collection Coordinators**	**<u>PDT Lead:</u>** **USACE - Murrell** **<u>PDT Members:</u>** **To be determined by leads.**

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

Temporary Housing and Roofing Out-brief

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Flood Risk Management Out-brief

US Army Corps of Engineers

Flood Risk Management

FEMA

Issue: FRM-1	Proposed COA/Timeline	Lead/PDT
What are the successes and lessons learned to date from the Regional Interagency Levee Task Force (ILTF)? Successes: • Improved communication among federal, state, and local agencies. • Addressed damaged levees, but also considered and evaluated non-structural alternatives (NSAs) and other mitigation solutions. • Improved service to flood victims. • Identifying potential policy and program improvement opportunities.	Key Lessons Learned: • Need high level of commitment from agency leadership. • Need adequate funding to support an interagency effort and information outreach. • Closer pre-disaster coordination between agencies and state programs is required (data sharing). • ILTF activities should expand to include state and local flood mitigation plans. • Early ILTF implementation and education. Constraints: • Existing authorities focus on near-term solutions. • The mindset of the sponsor that the preferred solution is a structural repair vice a NSA. • Short-term recovery / rehabilitation activities override consideration of longer term non-structural mitigation alternatives.	Recommendations: • Use existing ILTF structure & documents to formalize an SOP for future ILTFs that incorporates lessons learned and addresses constraints. Lead: Bruce Munholand; Members: ILTF & ILWGs; Priority: Long term. • Increase education and outreach through development of a comprehensive communications plan. Lead: Candice Walters; Larry Buss; Members: Selected ILTF members;

US Army Corps of Engineers

Flood Risk Management

FEMA

Issue: FRM-2	Proposed COA/Timeline	Lead/PDT
Should the Regional ILTF concept transition to long-term forum? • **If so, what should the structure look like, what organizations are involved, what is its mission, and how are existing state/regional groups integrated?** <u>Key Discussion Points</u>: • Need for interagency disaster recovery structure and long-term interagency flood risk management organization (at state and regional levels). • Silver Jackets concept for implementation at the state and/or regional level. • More local involvement (must be a bottom up effort). • Use of existing state / regional organizational structures. • Information sharing among partners. • Need for long-term watershed and regional planning. • Name change from levee focus to foster greater participation. • Move from reactive to proactive	<u>Recommendations</u>: • Continue to establish a formal ILTF structure after major floods to facilitate coordinated recovery of flood damage reduction systems / NSAs. • Develop a coordinated federal / state concept for a long-term state-level partnerships (Silver Jackets). – State priority focused – Complement existing state level entities – Focus on initial opportunities for collaboration on flood risk management (e.g. *MapMod, Mitigation Planning*) • Develop an appropriate regional framework and partnerships to address long-term regional flood risk management issues. – Continue ILTF initiatives and NSAs	This will be implemented through establishment of the SOP (FRM-1). Leads: Jennifer Dunn; Norb Schwartz; Bob Bissell; State Reps (TBD); Members: Selected ILWG and ILTF members; Priority: Long term. Lead: TBD; Members: ILTF Flood Risk Management Committee; Priority: Long term.

US Army Corps of Engineers

Flood Risk Management

FEMA

Issue: FRM-3	Proposed COA/Timeline	Lead/PDT
Policy issues – Can we identify agency policy issues that should be reviewed / addressed for agencies involved in the ILTF process and flood risk management? Key Discussion Points: • Increased ability to evaluate / implement NSAs. • Requirement for flood mitigation plans (link PL84-99 work to mitigation plans). • ILTF PgMP in sync with state mitigation plan. • Require flood insurance in leveed areas. • Retaining assistance eligibility for NSAs. • Resilient features; levee setbacks; controlled flooding; deliberate	Recommendations: • Establishing a process in the ILTF to identify policy issues and make recommendations to participating agencies. – Policy White Papers – Ongoing NSA evaluations • FEMA / USACE revise state and local mitigation guidelines to incorporate levee systems; coordinate with FEMA PA.	Lead: ILTF; Members: ILTF members; Priority: Long term. Leads: Deb Ingram; Norb Schwartz; Bob Bissell; Jeff Jensen; Priority: Long term.

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Q & A's:

Flood Risk Management Breakout Outbrief

US Army Corps of Engineers

FEMA

2008 USACE/FEMA RAP Workshop

US Army Corps of Engineers

FEMA

USACE/FEMA RAP Workshop Objectives

- Establish status of key national/intergovernmental planning and preparedness initiatives/actions developed prior to and during the past year in terms of successes and shortfalls and evaluate progress. Desired End State: 2009 Readiness Snapshot
- Determine priorities for intergovernmental remedial actions required to build and/or enhance existing capabilities to respond to major disasters. Desired End State: Intergovernmental RAP Plan of Action.
- Determine where policy or doctrinal adjustments are required to improve federal readiness and mission execution. Desired End State: Framework for 2009 Senior Leaders' Seminar.

US Army Corps of Engineers

USACE/FEMA 2008 RAP Workshop

FEMA

Closing Remarks

US Army Corps
of Engineers

FEMA

USACE Remedial Action Program:

https://eportal.usace.army.mil/sites/RSC/CERAP

National Exercise Schedule:

HSEEP.DHS.GOV
